


SIGN OFF / APPROVAL

Process Workflow


دائرة الثقافة والسياحة
DEPARTMENT OF CULTURE
AND TOURISM




Project:	Business Processes	Reference No:	BP/CMW/02
Subject for Sign Off: Change Management Workflow (Process and Forms)			
Basis of Sign Off: Attached the following Process documents and Forms for Change Management Process for your acceptance. - Change Management Workflow - Variation Request (VR) - Engineer's / Employer's Instruction (EI) - Post Award Change Order Form (PACOF) - Variation Order (VO)			
Project Management and Engineering: Director	Name:	Said Ali Al Khatib	
	Signature:		
	Date:	24/4/2019	
Tendering and Projects Control Director	Name:	Khader Abu Ghannam	
	Signature:		
	Date:	21/5/2019	



Change Management Workflow

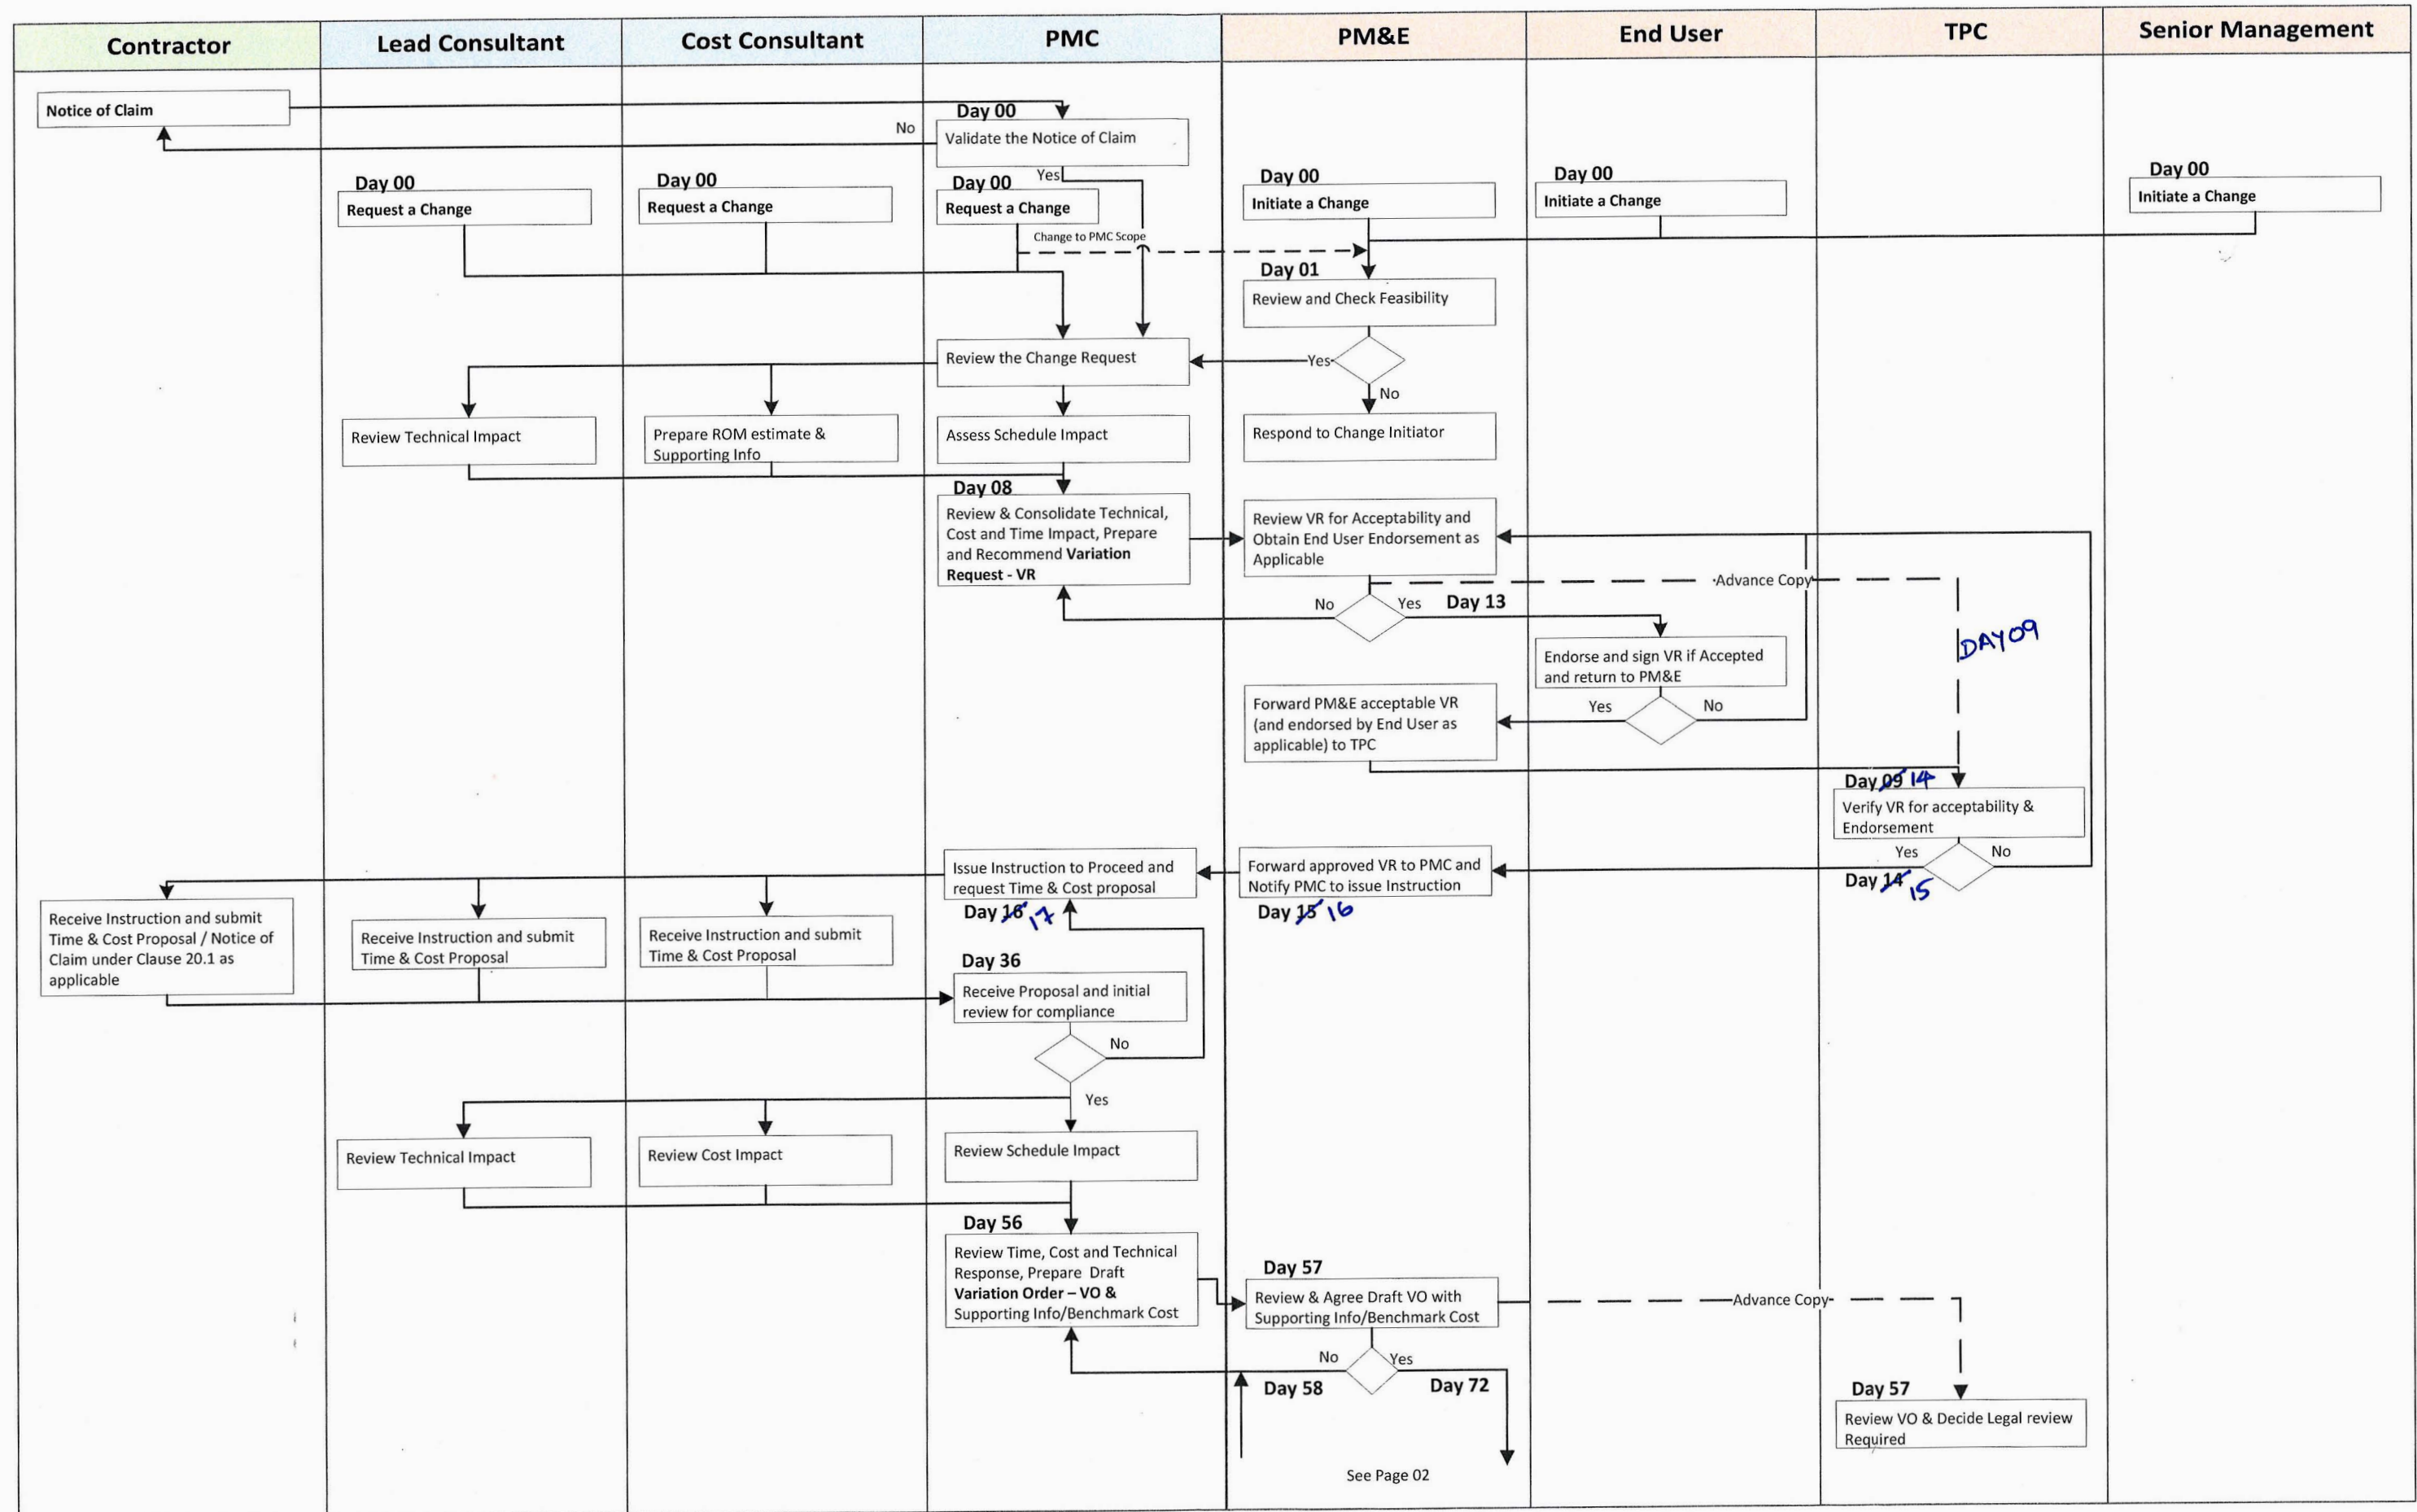

Change Management Workflow

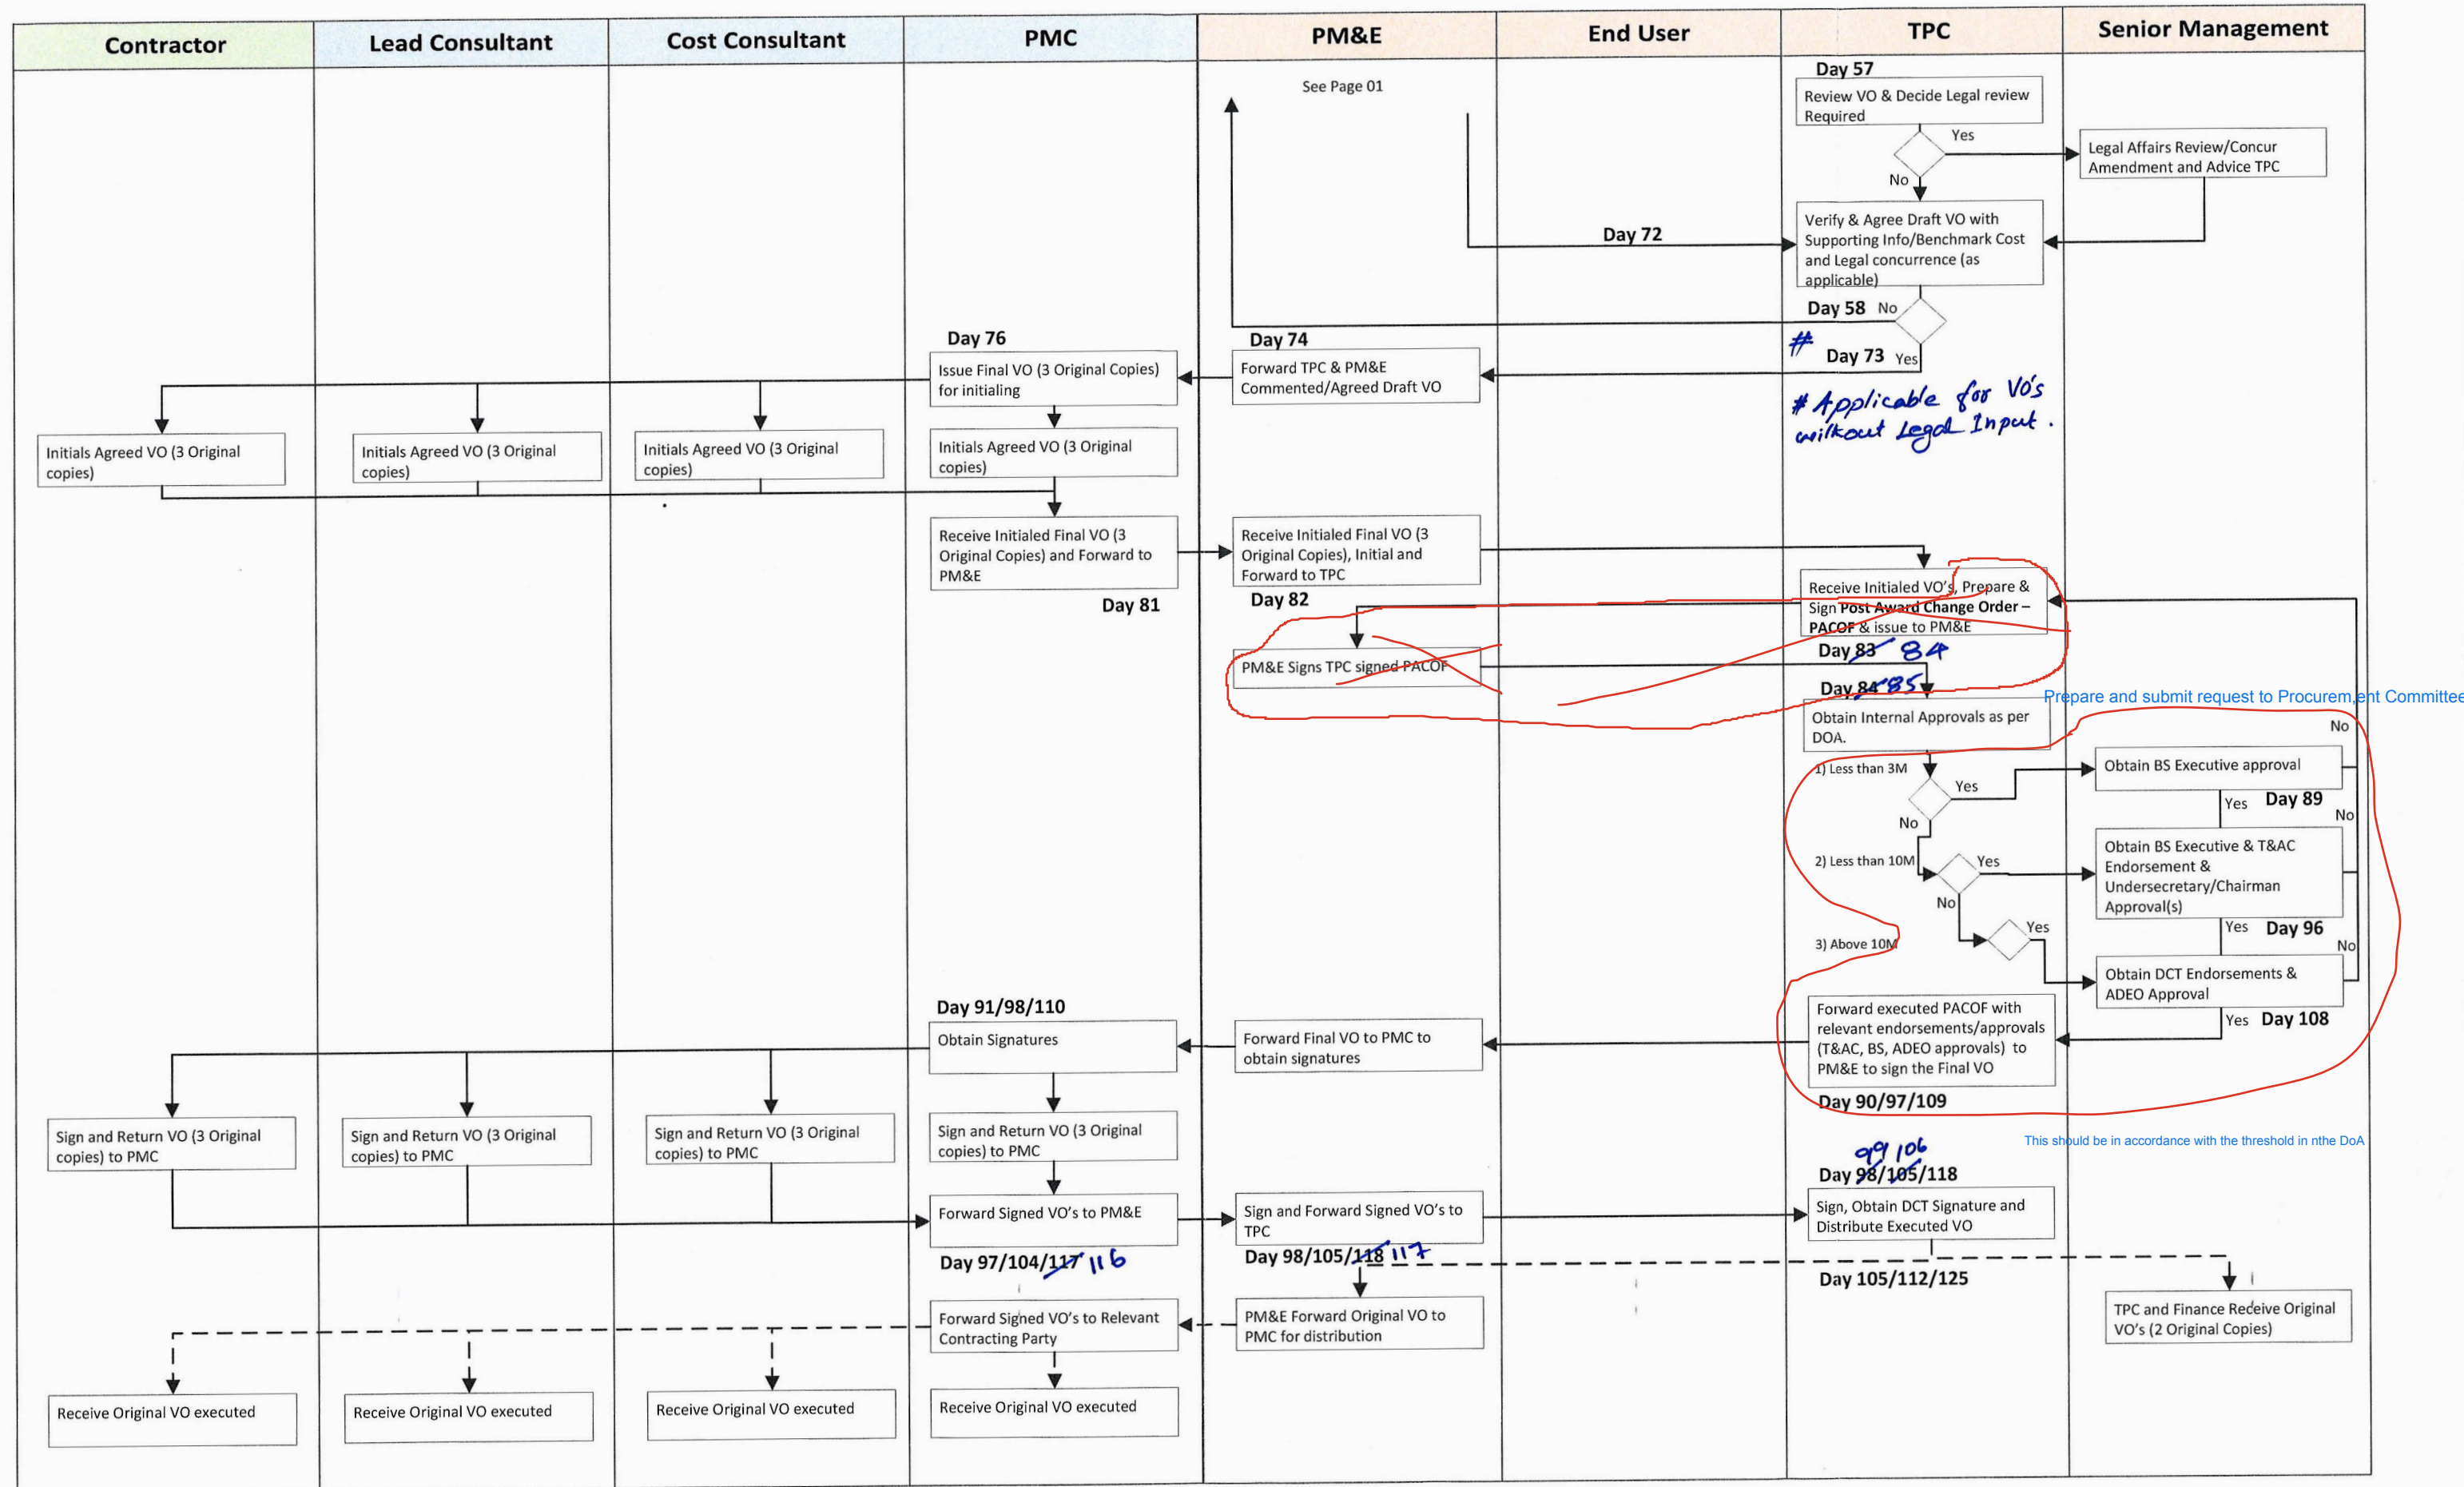

VARIATION REQUEST

Project:	Reference No: VR---									
Description of Change: [insert details]										
Reason for Change: <table style="width: 100%; border: none;"> <tr> <td style="width: 33%;">Client Change ☐</td> <td style="width: 33%;">Design Development ☐</td> <td style="width: 33%;">Site Conditions ☐</td> </tr> <tr> <td>Statutory Requirements ☐</td> <td>Tenant Requirement ☐</td> <td>Provisional Sum ☐</td> </tr> <tr> <td>Other ☐</td> <td colspan="2">Please specify</td> </tr> </table>		Client Change ☐	Design Development ☐	Site Conditions ☐	Statutory Requirements ☐	Tenant Requirement ☐	Provisional Sum ☐	Other ☐	Please specify	
Client Change ☐	Design Development ☐	Site Conditions ☐								
Statutory Requirements ☐	Tenant Requirement ☐	Provisional Sum ☐								
Other ☐	Please specify									
Cost and Time Impact: Estimated Time Impact (Days): Estimated Cost Impact (AED): <table style="width: 100%; border: none;"> <tr> <td style="width: 40%;">Professional Fee(s):</td> <td style="width: 10%;">Included ☐</td> <td style="width: 10%;">Excluded ☐</td> </tr> <tr> <td>Basis of Estimate(s):</td> <td>QS Estimate ☐</td> <td>Con. Estimate/Quotation ☐</td> </tr> <tr> <td>Source of Funding:</td> <td>Contingency ☐</td> <td>Budget Increase ☐</td> </tr> </table>		Professional Fee(s):	Included ☐	Excluded ☐	Basis of Estimate(s):	QS Estimate ☐	Con. Estimate/Quotation ☐	Source of Funding:	Contingency ☐	Budget Increase ☐
Professional Fee(s):	Included ☐	Excluded ☐								
Basis of Estimate(s):	QS Estimate ☐	Con. Estimate/Quotation ☐								
Source of Funding:	Contingency ☐	Budget Increase ☐								
Quality Assessment: <i>Design assessment of proposed change, including functionality, durability, maintainability, etc</i>										
Recommended by: <table style="width: 100%; border: none;"> <tr> <td style="width: 35%;">Project Manager: [insert]</td> <td style="width: 15%;">Name:</td> <td style="width: 50%; border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Signature:</td> <td style="border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Date:</td> <td style="border-bottom: 1px solid black;"></td> </tr> </table>		Project Manager: [insert]	Name:			Signature:			Date:	
Project Manager: [insert]	Name:									
	Signature:									
	Date:									
Endorsed by : <table style="width: 100%; border: none;"> <tr> <td style="width: 35%;">End User Representative: [insert]</td> <td style="width: 15%;">Name:</td> <td style="width: 50%; border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Signature:</td> <td style="border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Date:</td> <td style="border-bottom: 1px solid black;"></td> </tr> </table>		End User Representative: [insert]	Name:			Signature:			Date:	
End User Representative: [insert]	Name:									
	Signature:									
	Date:									
Approved by: <table style="width: 100%; border: none;"> <tr> <td style="width: 35%;">Director of PM&E: (PM&E Department)</td> <td style="width: 15%;">Name:</td> <td style="width: 50%; border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Signature:</td> <td style="border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Date:</td> <td style="border-bottom: 1px solid black;"></td> </tr> </table>		Director of PM&E: (PM&E Department)	Name:			Signature:			Date:	
Director of PM&E: (PM&E Department)	Name:									
	Signature:									
	Date:									
Verified by: <table style="width: 100%; border: none;"> <tr> <td style="width: 35%;">Director of TPC: (TPC Department)</td> <td style="width: 15%;">Name:</td> <td style="width: 50%; border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Signature:</td> <td style="border-bottom: 1px solid black;"></td> </tr> <tr> <td></td> <td>Date:</td> <td style="border-bottom: 1px solid black;"></td> </tr> </table>		Director of TPC: (TPC Department)	Name:			Signature:			Date:	
Director of TPC: (TPC Department)	Name:									
	Signature:									
	Date:									

Engineer's Instruction
(Sub-Clause 3.3)

دائرة الثقافة والسياحة
DEPARTMENT OF CULTURE
AND TOURISM



Employer: Department of Culture and Tourism
Address: [insert PO Box]
[insert City]
United Arab Emirates

Contract Ref:

ANNEXURE 2

Contract Dated:

Contract Amount:

Contract Period:

Instruction No:

Project: [insert Project Name]
Contract: [insert Contract Title]

Contractor: [insert contractor]
Address: [insert PO Box]
[insert City]
United Arab Emirates

Issue Date:

Pursuant to Sub-Clause 3.3 (Employer's Instructions), [insert contractor] (the "Contractor") is hereby instructed as follows:

1) xxx

xxx

If the above Instruction constitutes a Variation, then Clause 13 (Variations and Adjustments) shall apply.

Signed: _____
on behalf of [insert company]

Distribution: ☒ Employer ☒ Cost Consultant ☒ Principal Design Consultant
☐ Consultant of Record ☒ Contractor

Handwritten signature and date 17/04

Form No.: PC-TO-34
Rev. No.: 10
Effective Date: 21-Jun-2017
Page No.: 1 of 1

دائرة الثقافة والسياحة
DEPARTMENT OF CULTURE
AND TOURISM



Submission Details					
Agreement/PO Title: _____			Date: _____		
End User Name: _____			User/Requester Division: _____		
Supplier: _____			Award Recommendation Date: _____		
PR Number: _____			PR Approval Date: _____		
PR Value: _____ -			PO Number: _____		
Agreement Number: _____			Variation Order (VO) Number: _____		
Change Requested					
Change to Agreement Value	Original Agreement/PO Value:		AED		
	Previous VOs (if applicable)		AED		0.00
	Additional Value of this VO:		AED		0.00
	% Cumulative Change over Original Agreement Value:		%		
	Revised Agreement Value:		AED		0.00
	Budget availability confirmed?		Yes/No		YES
Change to Agreement Duration	Original Agreement Duration:		From	0-Jan-00	to 0-Jan-00
	Previous Variation Orders (if applicable)		From	-	to -
	Proposed Duration of this CO:		From	1-Jan-00	to 0-Jan-00
	% Cumulative Change over Original Agreement Duration		%		0.0%
	Revised Agreement Duration:		From	0-Jan-00	to 0-Jan-00
Notes :					
Attachments:					
Recommendation, Review and Endorsement					
End User (Project Management & Engineering)			Tendering and Projects Control		
Project Manager		Director	Manager - Contracts Admin		Director
Name: _____		Name: Said Ali Al Khatib	Name: Jayagopalan U		Name: Khader Abu Ghannam
Signature: _____		Signature: _____	Signature: _____		Signature: _____
Date: _____		Date: _____	Date: _____		Date: _____
Approvals - Up to AED 3 million					
Executive Director Joint Business Support (approval authority up to AED 3 million)			Signature: _____		Not applicable ☐
			Date: _____		Approve ☐
					Reject ☐
Further Recommendation, Review and Endorsement - above AED 3 million					
Tender & Auctions Committee			Signature: _____		Approve ☐
			Date: _____		Reject ☐



VARIATION ORDER (VO)

Contract Details			
Project : XX	Agreement Ref / Nr : Contract Stage :		
Agreement Title : XX			
Contracting Party :			
Cost and Schedule prior to this Variation Order			
Contract Value :	Commencement date :		
Approved VOs (nr) :	Time for completion :		
Approved VOs (Value) :	Approved extensions :		
Revised Contract Value : -	Revised completion date :		
Variation Details			
VO Nr : 00		Subject :	
<u>Brief description</u> : Under the terms of the above referenced Agreement, the following variation (s) is agreed: FORMAT ONLY Except as otherwise stated in this Variation Order and / or previous Variation Orders, all other terms and conditions of the above referenced Contract shall remain unchanged and in full effect.			
Value of this VO :	Lump Sum		
Revised Contract Value :	AED 0.00	Lump Sum	
Following this VO			
Method of payment :			
Schedule impact :	0		
Revised Completion Date :	00-Jan-00		
Acceptance by the Contracting Party			
0			
Authorised Signatory	_____		
Designation	_____		
Signature & Date	_____		
Recommendation			
Authorised Signatory	_____		
Designation	_____		
Signature & Date	_____		
Approvals			
DCT Project Management & Engineering		DCT Tendering & Projects Control	
Project Manager	_____	Contracts Manager	Jayagopalan U
Signature & Date	_____	Signature & Date	_____
Director	Said Al Khatib	Director	Khader Abu Ghannam
Signature & Date	_____	Signature & Date	_____
DCT Authorised Signatory			
Director General	Saif Saeed Ghobash	DCT Stamp	
Signature & Date	_____		

#

Appendix A: Detailed Scope of Services

#

Appendix C: Related correspondence

#

Appendix B: Schedule of Lump-Sum and Cash flow / Payment schedule

As applicable.

17/01/20

XX

XX

Variation Order Nr 00

Appendix A: Detailed Scope of Services

As applicable

XX

XX

Variation Order Nr 00

Appendix B: Schedule of Lump-Sum and Cash flow / Payment schedule

Sr nr	Item Description	Amount (AED)
1		
2		
3		
4		
5		
6		
7		
Total Lump-Sum fees		-

XX

XX

Variation Order Nr 00

Appendix C: Related Correspondence



CONTRACT VARIATIONS

COST BENCHMARKING REQUEST

Original Contract Details

Project : Agreement Ref :
 Agreement Title : Contracting Party :
 BM REF : Date :

Scope of Varied Works

Headline Scope : [Title of the scope to identify the major Works]
 Detailed Scope : [Include a brief narrative of the scope - use additional sheet if required]
 Month & year of the Works : [Insert the time of the Works executed / to be executed]
 Duration of the Works : [Insert the actual / estimated duration of the proposed Works]
 Scope basis : [Specify whether the works are based on Tender / Engineer's Instruction / Claims etc.]
 Scope basis Ref : [Insert Tender No. / EI ref. / Claim Ref. etc.]
 Drawings / Specifications for the Scope : [Attach relevant drawings / photos / images clearly indicating the location and scope of Works]

Commercial Evaluation

Method of Valuation : Competitive Tender / Contract Rates / New rates / Quotations [As appropriate]

Valuation Details

Competitive Tender		Contract Rates / New rates / Quotations	
No. Bidders	: [Should be 3 bidders as a minimum]	Contractor's Proposed	AED xx
Commercial offer amounts	: [Specify amounts quoted by all bidders]	%age value using Contract	
Name & Address of selected bidder	: [Name and address of the selected Bidder]	%age value using New rates	
Final offer amount	: [Final offer amount from Bidder]		
Engineer assessed value	: [Insert Engineer's assessment amount]	[Insert Engineer's assessment amount]	
Engineer's comments and recommendations	: [Engineer / Cost consultant to complete the comparison summary included in Appendix A along with relevant substantiations for the recommended rates]		
Engineer / PMC comments / recommendations	: [specific recommendation for the amount /bidder]		

Recommendation

Engineer / PMC Representative : xxx
 Signature : _____ Date _____

DCT Approvals

Manager, Contracts Admin & Cost Estimation	: Jayagopalan Ullattil	DCT Project Manager
Signature & Date	: _____	Signature & Date
TPC Director	: Khader Abu Ghannam	
Signature & Date	: _____	
Comments	: _____	
